

Work Order ID 121505

121505

Page 1

Thursday, June 26, 2014 3:01:50 PM

Item ID: D350-748-101

Accept

N900040100

Setup Start *NS1*

Revision ID:

Stop *NS2*

Item Name: Fwd Crosstube

Start Date: 6/03/14 Start Qty: 1.00

1

Cust Item ID:

Required Date: 7/15/14 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: MLJ

Date: 14-06-27 Tooling:

Date:

Run Start *NR1*

QC:

Date: SPC (Y/N):

Date:

Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D350-748-141	G

100	Document Control	0.00							
	DOCUMENT CONTROL								

100

DC

Doc.Control -USB or Paperwork

Memo

0.00

Photocopy bluefile & type labels per PPPD350-748-101

CHG003

FEB 11 2015

110

110

CNC Bend 1

CNC Delta 100 Bender

BENDING MACHINE - CROSSTUBES

Memo

0.00

Bend tube as per Dwg D350-748-141 using CNC bender program D350F and Folio FT

*****UNDHR BEND .225" PER SIDE*****

*****USE (4) DT9824 SHIM BLOC TO CHECK STRAIGHTNESS*****

RO

DQA:

Date: 15/03/18



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: ~~DRM~~

Date: 15/03/17

Work Order update only ☐

Work Order: <u>121505</u> Part No. <u>D350-748-101</u> NCR No. <u>15-4627</u>				DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☒ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☒ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector		
Design	14/11/3	110	1	ONE ANGLE IS UNDER TOLERANCE RC-BEND IN PROSS.	DAS 12 9-89 14/11/3	Acceptable.	DAS 12 9-89 14/11/3	S 14/11/3 OK	S 14/11/3		
Doc/Data											
Equip/Tooling											
Handling/Pre											
Material											
Operator											
Offset/Setup ☒											
Process ☒											
Supplier											
Training											
Transport											
Unapproved											

FAULT CATEGORY							
Landing Gear ☒ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube		General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function		☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence		☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other	

Work Order ID 121505

121505

Page 2

Thursday, June 26, 2014 3:01:50 PM

Item ID: D350-748-101

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Fwd Crosstube

Start Date: 6/03/14 Start Qty: 1.00

1

Cust Item ID:

Required Date: 7/15/14 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start

NR1

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

120

0.00

120

Crosstubes

Memo

0.00

Crosstubes

VERIFY CROSSTUBE DIMENSIONS AS PER DWG

Jo 14-10-29

125

0.00

125

Outsource1

Memo

0.00

Outsource process - Heat Treat

ISSUE P/O TO METCOR: 26301

Stress relief

Heat treat crosstube as per QSI010 4.3 within 12h after bending

CR 14/10/290

126

Receive & Inspect for Damage & Mat'l Certs

0.00

126

Packaging

Memo

0.00

Packaging

IX 8/14-10-31

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____ Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Work Order ID 121505

Thursday, June 26, 2014 3:01:50 PM

121505

Page 3

Item ID: D350-748-101

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Fwd Crosstube

Start Date: 6/03/14 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 7/15/14 Req'd Qty: 1.00 ***1***

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
127	QC15- Crosstube Dimensional Check	0.00							
127									
QC	Memo	0.00							
Quality Control	***MARK CUT LINES***								
128		0.00							
128									
Crosstubes	Memo	0.00							
Crosstubes	CUT TUBE AT HEIGHT ON FAI SHEET								
	VERF HEIGHT <u>23.100</u> BY QC 15 LEVEL INSPECTOR <u>Splulu10</u>								
	VERF TWIST <u>8.00</u> BY QC15 LEVEL INSPECTOR <u>Splulu10</u>								

DAS
03
9-88

14-11-10

14-11-10

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS <table style="width:100%;"> <tr> <td>Skid-tube ☐</td> <td>Crosstube ☐</td> <td>Water Jet ☐</td> <td>Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>	Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐															
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐															
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐															
Large Fab ☐	Composite ☐	Supplier ☐																

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design ☐									
Doc/Data ☐									
Equip/Tooling ☐									
Handling/Pre ☐									
Material ☐									
Operator ☐									
Offset/Setup ☐									
Process ☐									
Supplier ☐									
Training ☐									
Transport ☐									
Unapproved ☐									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Work Order ID 121505

Thursday, June 26, 2014 3:01:50 PM

121505

Page 4

Item ID: D350-748-101

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Fwd Crosstube

Start Date: 6/03/14 Start Qty: 1.00

1

Cust Item ID:

Required Date: 7/15/14 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

130

130

Crosstubes

Crosstubes

Crosstubes

Memo

0.00

0.00

2- Drill Tube as per Dwg D350-748-141 Using DT8876 A,B & C Drill Jigs,
Set-up drill table as per QSI 010

3- Deburr

4- Engrave Part # and Batch # as per Dwg D350-748-141

5- Remove all marks from tube within limits of D350-748-141

6- Apply a light coat of LPS3 on the interior of tube
Batch: _____

140

140

QC

Quality Control

QC5- Inspect part completeness to step on W/O

0.00

Memo

0.00

CHECK 10 DEG HOLES WITH DT8876E (EUROCOPTER CLAMP)

DAS
38
9-89

NOV 21 2014

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td>Skid-tube ☐</td> <td>Crosstube ☐</td> <td>Water Jet ☐</td> <td>Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>	Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐															
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐															
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐															
Large Fab ☐	Composite ☐	Supplier ☐																

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Work Order ID 121505

June-27-14 7:46:51 AM

121505

Page 5

Item ID: D350-748-101

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Fwd Crosstube

Start Date: 6/03/14

Start Qty: 1.00

1

Cust Item ID:

Required Date: 7/15/14

Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan:

Date:

Tooling:

Date:

Run

Start

NR1

QC:

Date:

SPC (Y/N):

Date:

Stop

NR2

Sequence ID/
Work Center ID

Operation
Description

Set Up/
Run Hours

Tool ID

Tool #

Plan
Code

Accept
Qty

Reject
Qty

Reject
Number

Insp.
Stamp

150

Outsource process-Cadplate per QSI017 4.1.9.1

0.00

150

Outsource3

Memo

0.00

Outsource process - Cad plate

Issue P/O: 26611

Stress relief at 375° for 5 hours

Magnetic Particle Inspect per ASTM E1444

Cadium Plate per AMS-QQ-P-416B, Class 1, Type 2

Embrittle relief at 375° for 8 hours, Chromate Treat

Possible Supplier: Southwest United Industries

Ensure Certificate of Conformity is attached

CL 14/11/25 ①

160

Receive & Inspect for Damage & Mat'l Certs

0.00

160

Packaging

Memo

0.00

Packaging

Ensure certificate of conformity is attached

IX 8015-01-27

170

QC5- Inspect part completeness to step on W/O

0.00

170

QC

Memo

0.00

Quality Control

D 15-01-23

DAS

9

9-89

Work Order ID 121505

Thursday, June 26, 2014 3:01:51 PM

121505

Page 6

Item ID: D350-748-101

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Fwd Crosstube

Start Date: 6/03/14

Start Qty: 1.00

1

Cust Item ID:

Required Date: 7/15/14

Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan: _____

Date: _____

Tooling: _____

Date: _____

Run

Start

NR1

QC: _____

Date: _____

SPC (Y/N): _____

Date: _____

Stop

NR2Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

174

Outsource process - NDT per QSI038 4.1

0.00

174

Outsource2

Memo

0.00

Outsource process - NDT

ISSUE P/O TO ACUREN: 27244OK 15/01/29 ①

176

Receive & Inspect for Damage & Mat'l Certs

0.00

176

Packaging

Memo

0.00

Packaging

IX SP 15-01-29

178

QC5- Inspect part completeness to step on W/O

0.00

178

QC

Memo

0.00

Quality Control

DAS
38
9-89

JAN 30 2015

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Work Order ID 121505***121505***

Page 7

Thursday, June 26, 2014 3:01:51 PM

Item ID: D350-748-101

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Fwd Crosstube

Start Date: 6/03/14

Start Qty: 1.00

1

Cust Item ID:

Required Date: 7/15/14

Req'd Qty: 1.00

1

Customer:

Reference:

Run Start

NR1

Stop

NR2

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

180

0.00

180

SprayPaint

SprayPaint

1

Ch 15-02-02

Spray Painting

Memo

0.00

1-Prime inside and out crosstube as per QSI 005 4.2

BATCH: m 129807

2-Paint Outside of Tube as per Dart QSI 005 4.2

BATCH: 131 233

190

0.00

190

QC

Quality Control

QC14- Inspect Spray Paint

Memo

0.00

Then, Wrap in plastic bag to protect from scratches

1

DAS
38
9-8-99

15-02-09

Use Axalta
97
9-8-99
15-02-02
3.5 H.G

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td>Skid-tube ☐</td> <td>Crosstube ☐</td> <td>Water Jet ☐</td> <td>Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>	Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐															
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐															
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐															
Large Fab ☐	Composite ☐	Supplier ☐																

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design ☐									
Doc/Data ☐									
Equip/Tooling ☐									
Handling/Pre ☐									
Material ☐									
Operator ☐									
Offset/Setup ☐									
Process ☐									
Supplier ☐									
Training ☐									
Transport ☐									
Unapproved ☐									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

121505

Thursday, June 26, 2014 3:01:51 PM

Accept

N900040100

Setup Start *NS1*

Stop *NS2*

Item Name: Fwd Crosstube

Start Date: 6/03/14 **Start Qty:** 1.00 ***1***

Cust Item ID:

Required Date: 7/15/14 **Req'd Qty:** 1.00 ***1***

Customer:

Reference:

Run Start *NR1*

Approvals: _____ **Process Plan:** _____ **Date:** _____ **Tooling:** _____ **Date:** _____

Stop *NR2*

OC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

200

0.00

200

Crosstubes

0.00

Crosstubes

Crosstubes

Memo

INSTALL GROUND WIRE INSERT, THEN INSERT SCREW AND WASHER

1-Abrade mating surfaces of support and crosstube with 180 grit sandpaper, clean the area with MEK or equivalent as per dwg

2-Install supports with Proseal 890 per D350-748-141 and QSI 015

A/R Proseal 890 Batch: 130986
EXP: 6/15

3-Install supports clamps Using Dt8876 as per Dwg D350-748-141,Torque to 60-80 IN-LBS.

PROSEAL CURE TIME 72 HOURS:

Start: 15-2-3
Finish: 15-2-6

***RE-CHECK TORCQUE ON CLAMP AFTER PROSEAL HAS CURED
FOR 72HOURS AS PER DWG.***

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td>Skid-tube ☐</td> <td>Crosstube ☐</td> <td>Water Jet ☐</td> <td>Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>	Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Crosstube ☐	Water Jet ☐	Engineering ☐															
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐															
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐															
Large Fab ☐	Composite ☐	Supplier ☐																

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Work Order ID 121505

Thursday, June 26, 2014 3:01:51 PM

121505

Page 9

Item ID: D350-748-101

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Fwd Crosstube

Start Date: 6/03/14 Start Qty: 1.00

1

Cust Item ID:

Required Date: 7/15/14 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
210	QC5- Inspect part completeness to step on W/O	0.00				1			DAS 38 9-89
210									
QC	Memo	0.00							15-02-09
Quality Control	***RE-CHECK TORCQUE ON CLAMP AFTER PROSEAL HAS CURED FOR 72HOURS AS PER DWG.***								
220	Pick Kit	0.00							
220									
Packaging	Memo	0.00							DAS 26 9-89
Packaging									DAS 46 9-89
230	QC4- 100% Inspect kits for completeness	0.00							
230									
QC	Memo	0.00							DAS 66 9-89
Quality Control									

FEB 11 2015

FEB 11 2015

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other _____ _____ _____
--	--	---	---

Work Order ID 121505***121505***

Page 10

Thursday, June 26, 2014 3:01:51 PM

Item ID: D350-748-101

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Fwd Crosstube

Start Date: 6/03/14 Start Qty: 1.00

1

Cust Item ID:

Required Date: 7/15/14 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start

NR1

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

240

0.00

240

Packaging

Packaging

Memo

0.00

Identify and pack for shipping as per PPP D350-748-101

Location: 035

PPP Rev: _____

FEB 12 2015

DAS

46DAS
66
3-99

9-89

250

0.00

250

QC21 - Final Inspection - Work Order Release

QC

Memo

0.00

Quality Control

15/2/17 *[Signature]**mf**15-2-12*

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Picklist Print

Thursday, June 26, 2014 3:01:48 PM

Page 1

Work Order ID: 121505

121505

Parent Item: D350-748-101

D350-748-101

Parent Item Name: Fwd Crosstube

Start Date: 6/03/14

Required Date: 7/15/14

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP Rev:A New Issue 06-07-05 JLM
IPP Rev:B Update qty of MS21042L5 06-09-12 KJ VERIFY
BY:DD
IPP Rev:C Rev B 07-11-15 DD
IPP Rev D Combined manufacturing 08.04.02 EC verified by: DD
IPP Rev:E 08-06-24 revD as per dwg DD verified by:EC IPP Rev:F
10.08.04 added QSI010 4.3 DD verf:EC
IPP REV:G ADD UNDER BEND COMMENT 12-05-28 JLM IPP
REV:H 12.11.05 as per dwg D350-748-141G DD verf:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
AN4-41A		Purchased		No		220	Each	552.0000	8	(8)			DAS 26 9-89
AN4-41A									**	m130726			
Bolt													
					<u>Location</u>			<u>Loc Qty</u>		<u>Loc Code</u>			
					ST517			552					
					124241			2					
					124805			365					
					124836			185					
AN4-6A		Purchased		No		220	Each	2,305.000	16	(16)			DAS 26 9-89
AN4-6A									**	m126317		FEB 11 2015	
BOLT													
					<u>Location</u>			<u>Loc Qty</u>		<u>Loc Code</u>			
					ST355			604					
					16067			4					
					M128403			600					
					ST514			1701					
					M126317			350					
					M128634			1351					

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Picklist Print

Thursday, June 26, 2014 3:01:48 PM

Page 2

Work Order ID: 121505

121505

Parent Item: D350-748-101

D350-748-101

Parent Item Name: Fwd Crosstube

Start Date: 6/03/14

Required Date: 7/15/14

Start Qty: 1.00

Required Qty: 1.00

AN5-32A

Purchased

No

220

Each

310.0000

4

AN5-32A

Bolt

**

④

m130716

DAS
06
9-89

Location

Loc Qty

Loc Code

ST336

310

123523

4

124215

110

124805

4

m127363

4

m127550

30

m128403

8

m128634

150

DAS
46
9-89

DAS
28
9-89
FEB 11 2015

D3500-1

Manufactured

No

220

Each

41.0000

4

D3500-1

Saddle

**

4

DAS
06
9-89

Location

Loc Qty

Loc Code

ST

40

115746

40

ST430A

1

108799

1

B119743

4

DAS
46
9-89

DAS
28
9-89
FEB 11 2015

D3501-1

Manufactured

No

220

Each

768.0000

16

D3501-1

Bushing

**

16

DAS
06
9-89

Location

Loc Qty

Loc Code

ST046

768

117442

8

117505

60

119012

252

119635

206

120509

240

86913

2

Hex

DAS
46
9-89

DAS
28
9-89
FEB 11 2015

Thursday, June 26, 2014 3:01:48 PM

Shop Packet Print

Page 2

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Picklist Print

Thursday, June 26, 2014 3:01:49 PM

Page 3

Work Order ID: 121505

121505

Parent Item: D350-748-101

D350-748-101

Parent Item Name: Fwd Crosstube

Start Date: 6/03/14

Required Date: 7/15/14

Start Qty: 1.00

Required Qty: 1.00

MS21042L4

Purchased

No

220

Each

5,222.000

24

24

MS21042L 4

Locknut

**

m130799

DAS

26

9-89

DAS
26
9-89

Location

Loc Qty

Loc Code

ST307

5222

m126015

12

m126275

32

m127255

71

m127376

11

m127813

971

m128300

80

m128798

3045

m129472

1000

MS21042L5

Purchased

No

220

Each

1,156.000

4

4

MS21042L 5

Nut

**

m131340

DAS

26

9-89

DAS
26
9-89

Location

Loc Qty

Loc Code

ST307

1156

117611

1

125684

8

m127304

3

m127813

500

m128810

144

m129472

500

FEB 11 2015

DAS
26
9-89

Thursday, June 26, 2014 3:01:49 PM

Shop Packet Print

Page 3

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Picklist Print

Thursday, June 26, 2014 3:01:49 PM

Page 4

Work Order ID: 121505

121505

Parent Item: D350-748-101

D350-748-101

Parent Item Name: Fwd Crosstube

Start Date: 6/03/14

Required Date: 7/15/14

Start Qty: 1.00

Required Qty: 1.00

DAS
26
9-89

NAS1149D0463J

Purchased

No

220

Each

7,910.000

32

32

NAS1149D0463.J

WASHER

**

m/30799. DAS
46
9-89

DAS
26
9-89

Location

Loc Qty

Loc Code

ST277

7910

16941

8

M126221

20

M127813

22

M127904

1259

M128591

101

M128995

1500

M129390

5000

NAS1149D0563J

Purchased

No

220

Each

2,817.000

8

NAS1149D0563.J

Washer

**

DAS
26
9-89
m/30799 FEB 11 2015

DAS
26
9-89

Location

Loc Qty

Loc Code

GA

201

m125807

201

ST510a

2616

m126319

624

m128257

1992

D350-748-141TRN

Manufactured

No

110

Each

6.0000

1

1

D350-748-141TRN

Crosstube Turning Detail

**

B120396

① JW 14-10-29

Location

Loc Qty

Loc Code

LG

6

111544

1

112159

1

112160

1

112161

1

112163

1

112457

1

Thursday, June 26, 2014 3:01:49 PM

Shop Packet Print

Page 4

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Picklist Print

Thursday, June 26, 2014 3:01:49 PM

Page 5

Work Order ID: 121505

121505

Parent Item: D350-748-101

D350-748-101

Parent Item Name: Fwd Crosstube

Start Date: 6/03/14

Required Date: 7/15/14

Start Qty: 1.00

Required Qty: 1.00

D3502-1

Manufactured No

200

Each

85.0000

2

2

DAS

41

9-89

15-2-4

D3502-1

Support

Location

Loc Qty

Loc Code

LG

8

110785

8

LG050

77

104334

6

110283

13

113181

2

114329

12

94722

20

97212

12

99764

12

2

D3595-063-395

Manufactured No

200

Each

187.0000

2

2

DAS

41

9-89

15-2-4

D3595-063-395

Rubber Cushion

Location

Loc Qty

Loc Code

FG

5

87353

5

LG

106

110958

6

115027

100

LG051

20

114243

20

ST412

56

113105

56

2

Thursday, June 26, 2014 3:01:49 PM

Shop Packet Print

Page 5

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced ☐ Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Picklist Print

Thursday, June 26, 2014 3:01:49 PM

Page 6

Work Order ID: 121505

Parent Item: D350-748-101

Parent Item Name: Fwd Crosstube

121505

D350-748-101

Start Date: 6/03/14

Required Date: 7/15/14

Start Qty: 1.00

Required Qty: 1.00

ALS4-1032-225 AELS8-1032-225 Purchased

No

200

Each

491.0000

1

1

DAS

ALS4-1032-225

41

9-89

15-2-3

Rivnut

131067

Location

Loc Qty

Loc Code

FG

30

M127028

30

ST267

461

M127028

10

M127092

26

M128179

238

M128649

187

NAS1149D0363J

Purchased

No

200

Each

3,188.000

1

1

DAS

NAS1149D0363J

41

9-89

15-2-3

Washer

Location

Loc Qty

Loc Code

GA

23

124392

23

ST510a

3165

m126319

6

m128429

3159

MS21920-22

Purchased

No

200

Each

214.0000

2

2

DAS

MS21920-22

41

9-89

15-2-4

Clamp

Location

Loc Qty

Loc Code

LG

200

M128636

200

LG050

14

M127255

14

Thursday, June 26, 2014 3:01:50 PM

Shop Packet Print

Page 6

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐
--	--	---

Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

Picklist Print

Thursday, June 26, 2014 3:01:50 PM

Page 7

Work Order ID: 121505

121505

Parent Item: D350-748-101

D350-748-101

Parent Item Name: Fwd Crosstube

Start Date: 6/03/14

Required Date: 7/15/14

Start Qty: 1.00

Required Qty: 1.00

MS27039-1-10

Purchased

No

200

Each

956.0000

1

1

MS27039-1-10

SCREW

DAS

41

9-89

15-2-3

Location

Loc Qty

Loc Code

ST290

956

m126474

1

m127993

39

m128401

78

m128635

588

m129541

250

Thursday, June 26, 2014 3:01:50 PM

Shop Packet Print

Page 7

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS <table style="width: 100%;"> <tr> <td style="width: 33%;"> Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ </td> <td style="width: 33%;"> Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐ </td> <td style="width: 33%;"> Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ </td> <td style="width: 33%;"> Engineering ☐ Quality ☐ Other ☐ </td> </tr> </table>	Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐	Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐	Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐	Engineering ☐ Quality ☐ Other ☐
Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐	Crosstube ☐ Small Fab ☐ Finishing ☐ Composite ☐	Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐	Engineering ☐ Quality ☐ Other ☐			


Root Cause	Date	Step	Qty	Description of work order update or non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector
Design									
Doc/Data									
Equip/Tooling									
Handling/Pre									
Material									
Operator									
Offset/Setup									
Process									
Supplier									
Training									
Transport									
Unapproved									

FAULT CATEGORY

Landing Gear ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Inspection Strip in Tube ☐ Marks/Chatter ☐ Turning Sequence ☐ Wave/Twist in Tube	General ☐ Bend ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Burrs ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Drawing ☐ Drill Holes ☐ Finish ☐ Fit/Function	☐ Folio/Program ☐ Grain ☐ Hardware ☐ Inspection Incomplete/Unqualified ☐ Instructions Incomplete/Unclear ☐ Misaligned/off center ☐ Mislabeled ☐ Misread ☐ Off-set ☐ Out of Calibration ☐ Out of Sequence	☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Positioned Wrong ☐ Power Loss/Surge ☐ Pressure/Forced Set-up ☐ Temperature/Cure ☐ Weld ☐ Wrong Stock Pulled ☐ Other
--	--	---	--

DART AEROSPACE LTD		Work Order:	121505
Description: Crosstube High Fwd (AS350/355)		Part Number:	D350-748-101
Inspection Dwg: D350-748-141	Rev: G	Page 1 of 1	

Required Dimension	Min	Max
Height	23.12	23.38
1/2 Span	40.77	41.03
Angle	75	77
Total Span	81.55	82.05
Bending Passes	7	--
Crushing	--	7%
Twist	--	0.38

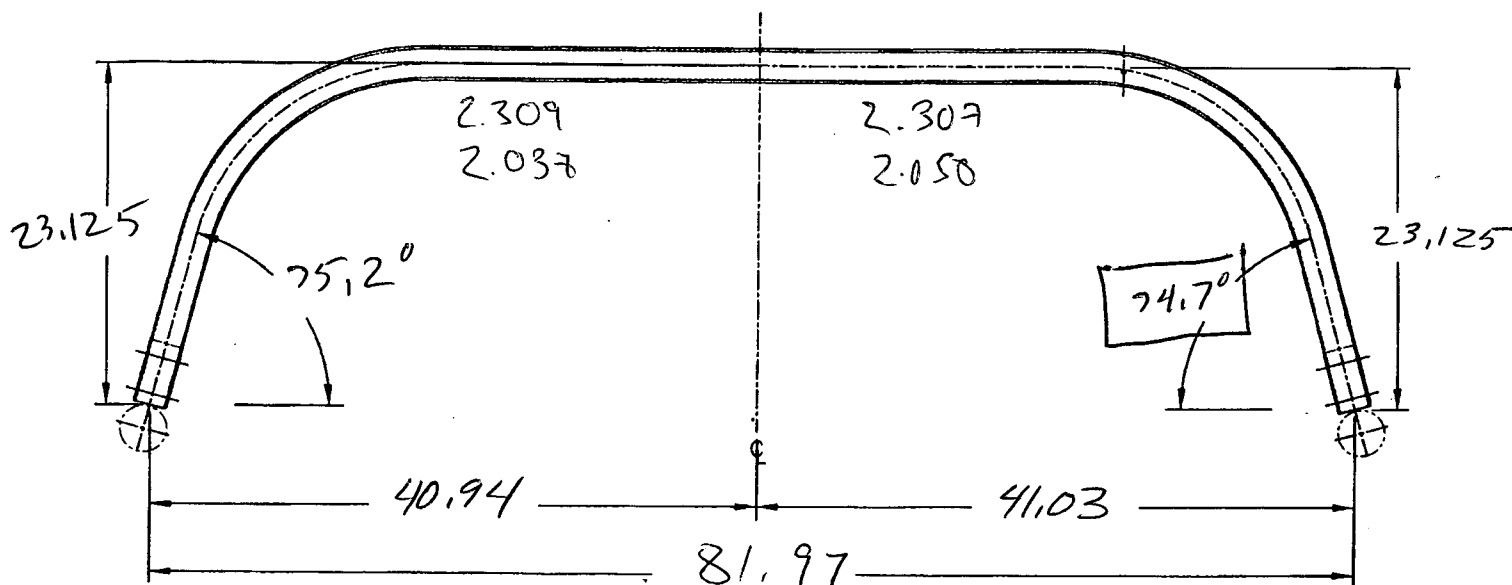

	Side A	Side B
Bending Passes	38	35
Crushing	5.8% 6.1%	5.8% 5.8%
Comments		

QC15 Inspection	14-11-10
Date	

Rev	Date	Change	Revised by	Approved
A	07.02.06	New Issue	KJ/JM	
B	10.08.23	Dwg Rev updated	KJ	
C	11.11.07	Dwg Rev updated	KJ	
D	12.04.16	Added bending, crushing & twist dimensions	KJ	
E	13.02.27	Dwg Rev updated	KJ	
F	14.02.13	Crushing & twist dimensions revised	KJ	

Item	Qty -141	Part Number	Description
1	X	D350-748-141	CROSSTUBE ASSEMBLY (AS 350/355 HI FWD)
2	1	D6015-125	CROSSTUBE (OR D6017-115)
3	2	D3502-1	SUPPORT
4	2	D3595-063-395	RUBBER CUSHION
5	1	AELS-1032-225	INSERT
6	1	NAS1149D0363J	WASHER (OR AN960JD10)
7	2	MS21920-22 OR MS 21920-21	CLAMP (PER DART SPEC. M-MS21920-21/-22)
8	1	MS27039-1-10	SCREW
9	A/R	PROSEAL 890 B-2	SEALANT, AMS-S-8802 CLASS B-2

GENERAL NOTES:

- 1) MATERIAL: MANUFACTURED FROM D6015-125 OR D6017-115
FINISHED LENGTH AFTER TURNING = 112.270 ± 0.06 (AFTER BENDING/TRIMMING = 110.27 REF)
- 2) FINISH: MAGNETIC PARTICLE INSPECT PER DART QSI 038 4.2
CADMIUM PLATE PER AMS-QQ-P-416B, CLASS 1, TYPE II
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2
PAINT OUTSIDE PER DART QSI 005 4.2
- 3) TOLERANCE: PER DART QSI 018 UNLESS OTHERWISE NOTED.
WALL THICKNESS ECCENTRICITY PER DART QSI 038 7.2
MIN. ALLOWABLE WALL IS -0.020 FROM NOMINAL
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED.
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX.
- 6) IDENTIFICATION: DART PART NUMBER 'D350-748-141' AND BATCH NUMBER ON INSIDE OF CUFF
PER DART QSI 044 6.4 (VIBRATING STYLUS)
- 7) WEIGHT: 30.45 lbs
- 8) PART IS SYMMETRIC ABOUT CENTERLINE, EXCEPT FOR Ø0.297 HOLE.
- 9) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE. WHEN DRILLING HOLES, EXTREME CARE MUST BE TAKEN AND CAREFUL DEBURRING PERFORMED TO ENSURE A CLEAN HOLE WITH NO CRACKING/CHIPPING/GROOVES.

TURNING

- 10) BLEND OUT ALL EDGES FROM MACHINING LONGITUDINALLY, TRANSITION SHOULD BE SMOOTH. NOTE: ALL HOLES ARE DRILLED AFTER BENDING.
- 11) HEAT TREAT TO MIN. 180 KSI PER MIL-T-6736 OR AMS2759/1E AFTER TURNING. ACCEPTABLE TO VERIFY TENSILE STRENGTH BY HARDNESS TEST PER ASTM E18 TO 40-45 HRC.

BENDING

- 12) ALL DIMENSIONS FOR BENT TUBE ARE POST STRESS RELIEF
- 13) BEND PROGRESSIVELY WITH A MINIMUM OF 7 PASSES PER SIDE. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 6% BASED ON O.D. ON TOP HALF OF BEND, AND 7% ON BOTTOM HALF OF BEND.
- 14) MAX AMPLITUDE OF RIBBLING ALONG BENT PORTION OF THE TUBE IS 0.030 (ZN A1-3)
- 15) AFTER BENDING, STRESS RELIEVE TUBE AT 650°F $\pm 0.25^\circ\text{F}$ FOR A MINIMUM OF 2 HRS AND ALLOW TO COOL TO AMBIENT TEMPERATURE (REF AMS2759/1E).
- 16) MAX TWIST AFTER STRESS RELIEF: WITH XTUBE LAYED FLAT ON SURFACE, THE DIFFERENCE BETWEEN CUFF HEIGHTS FROM THE SURFACE MAY BE NO LARGER THAN 0.38 (ZN C1-3).

ASSEMBLY

- 17) TO INSTALL D3502-1 SUPPORT: ABRASE MATING SURFACE OF SUPPORT AND CROSSTUBE WITH 180-GRIT SANDPAPER AND REMOVE RESIDUE WITH MEK (OR EQUIVALENT). APPLY A 0.02" TO 0.05" THICK LAYER OF PROSEAL 890 CLASS B-2 (OR AMS-S-8802 CLASS B-2) SEALANT TO MATING SURFACE OF SUPPORT.
- 18) TORQUE CLAMPS 60 TO 80 IN.-LB. ENSURE AT LEAST 1.5 THREADS SHOWING IN SAFETY AND THAT NUT HAS NOT BOTTOMED-OUT AFTER TORQUING. PRIOR TO PACKAGING, RE-CHECK TORQUE ON CLAMPS AFTER PROSEAL 890 SEALANT HAS CURED FOR 72 HOURS.

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER

NO. 121505 MLJ

1406-27

RELEASED
2012-11-01

G	RMV ABRASION STRIP, SUPPORT NOW W/ PROSEAL & CUSHION, ADD STRESS RELIEF, LONGER CUFF, NOW TRIMD AFTER BEND, ADD WALL DIMS & UPDATE TOL.	CP	12.09.12
F	ADD HRC TEST OPTION (B8-1) PER PAR 09-040, ADD TWIST LIMIT (A8-1, C1-3), ADD D6015-125 OPTION (C8-1), STOCK DIM NOW MACHINED (D1-4)	CP	10.11.23
E	REVISE GENERAL NOTES; UPDATE TO CURRENT ADD STANDARDS; RELOCATED FLAG #6 PER PAR 08-046 (ZN A6-3); TOLERANCES (ZN C6-3, D1-3)	RF	09.09.30
D	MAG. PARTICLE AND CAD PLATE AS MFD.	CP	06.10.31
C	ADD CAD PLATING	CP	06.08.14
B	ADD D6017-115 & PRIME AND PAINT	CP	06.06.30
A	NEW ISSUE	CP	08.03.31
REV.	DESCRIPTION	BY	DATE
DESIGN			
DRAWN			
CHECKED			
MFG. APPR.			
APPROVED			
DE APPR.			
DATE	12.09.12		

DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWING NO. D350-748-141	REV. G SHEET 1 OF 4
TITLE CROSSTUBE (AS 350/355 HI FWD)	SCALE NTS
COPYRIGHT © 2006 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR TRANSMITTED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD	

8 7 6 5 4 3 2 1

D

C

B


A

D


C

B

A

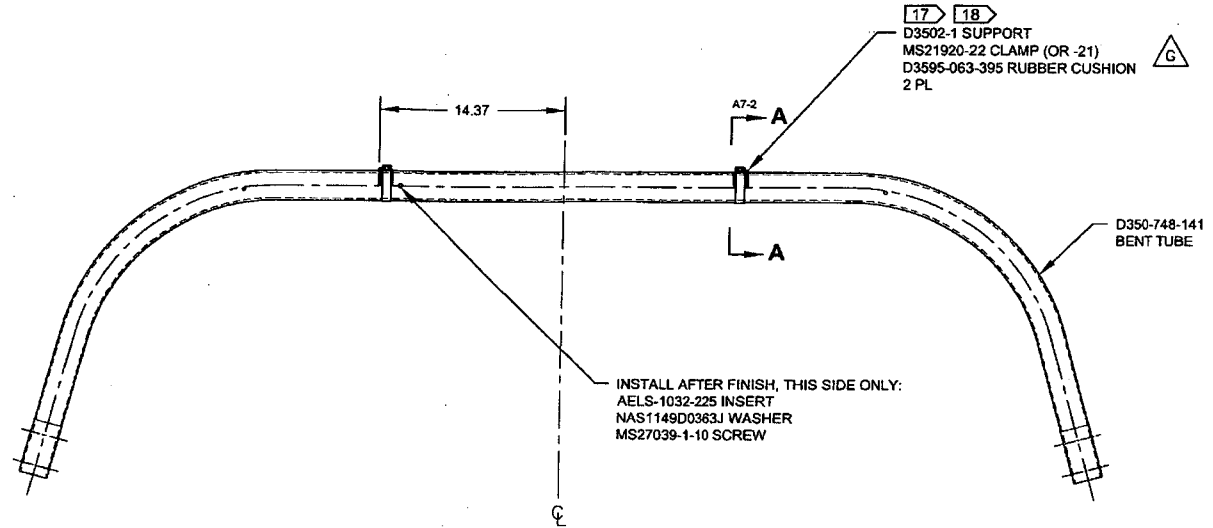

**D350-748-141
ASSEMBLY DETAIL**

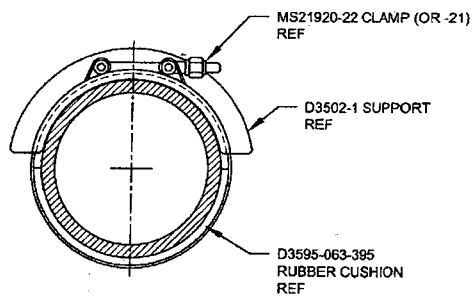


SECTION A-A D4-2
SCALE 6X




RELEASED
2012-11-01
WMP

DESIGN		DART AEROSPACE LTD	
DRAWN		HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. G
MFG. APPR.		D350-748-141	SHEET 2 OF 4
APPROVED		TITLE	SCALE
DE APPR.		CROSSTUBE (AS 350/355 HI FWD)	NTS
DATE	12.09.12	COPYRIGHT © 2006 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

8 7 6 5 4 3 2 1

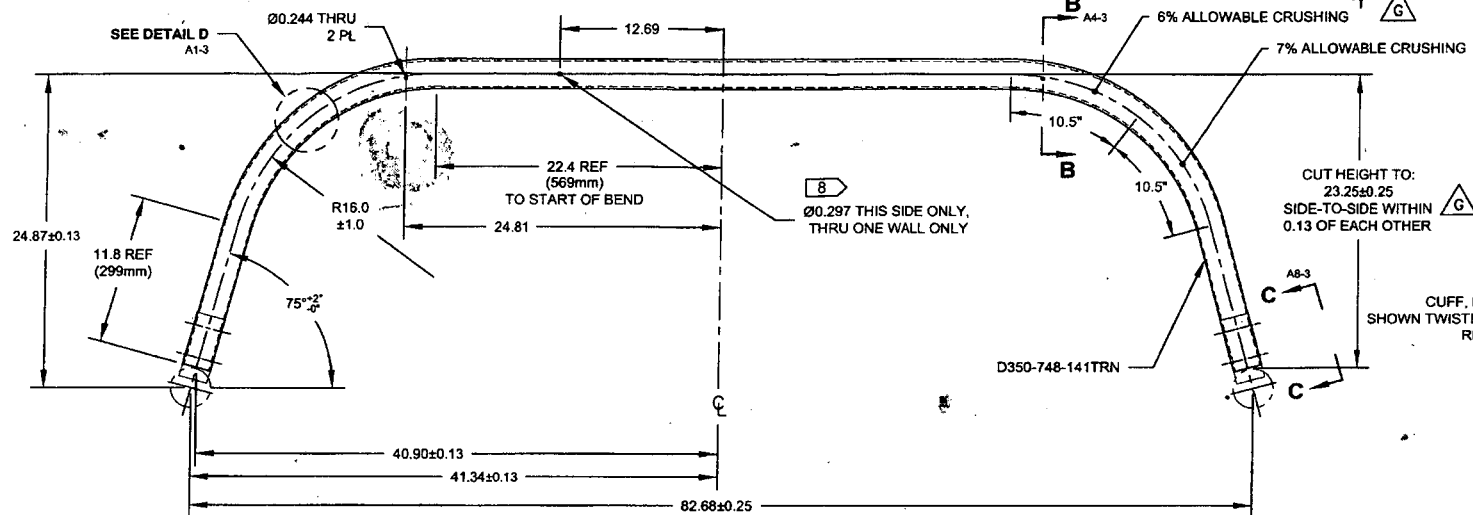


**D350-748-141
BENDING AND DRILLING DETAIL** 13

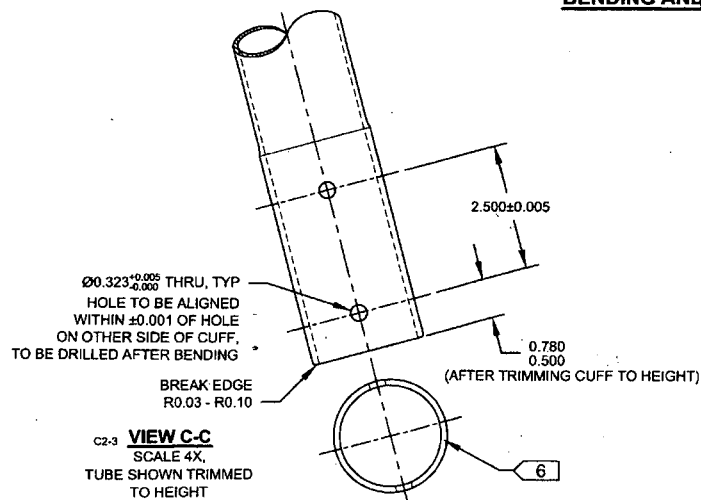


DESIGN		DART AEROSPACE LTD	
DRAWN		HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. G
MFG. APPR.		D350-748-141	SHEET 3 OF 4
APPROVED		TITLE	SCALE
DE APPR.		CROSSTUBE (AS 350/355 HI FWD)	NTS
DATE	12.09.12	COPYRIGHT © 2006 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR REPRODUCED IN ANY MANNER WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

RELEASED
2012-11-01

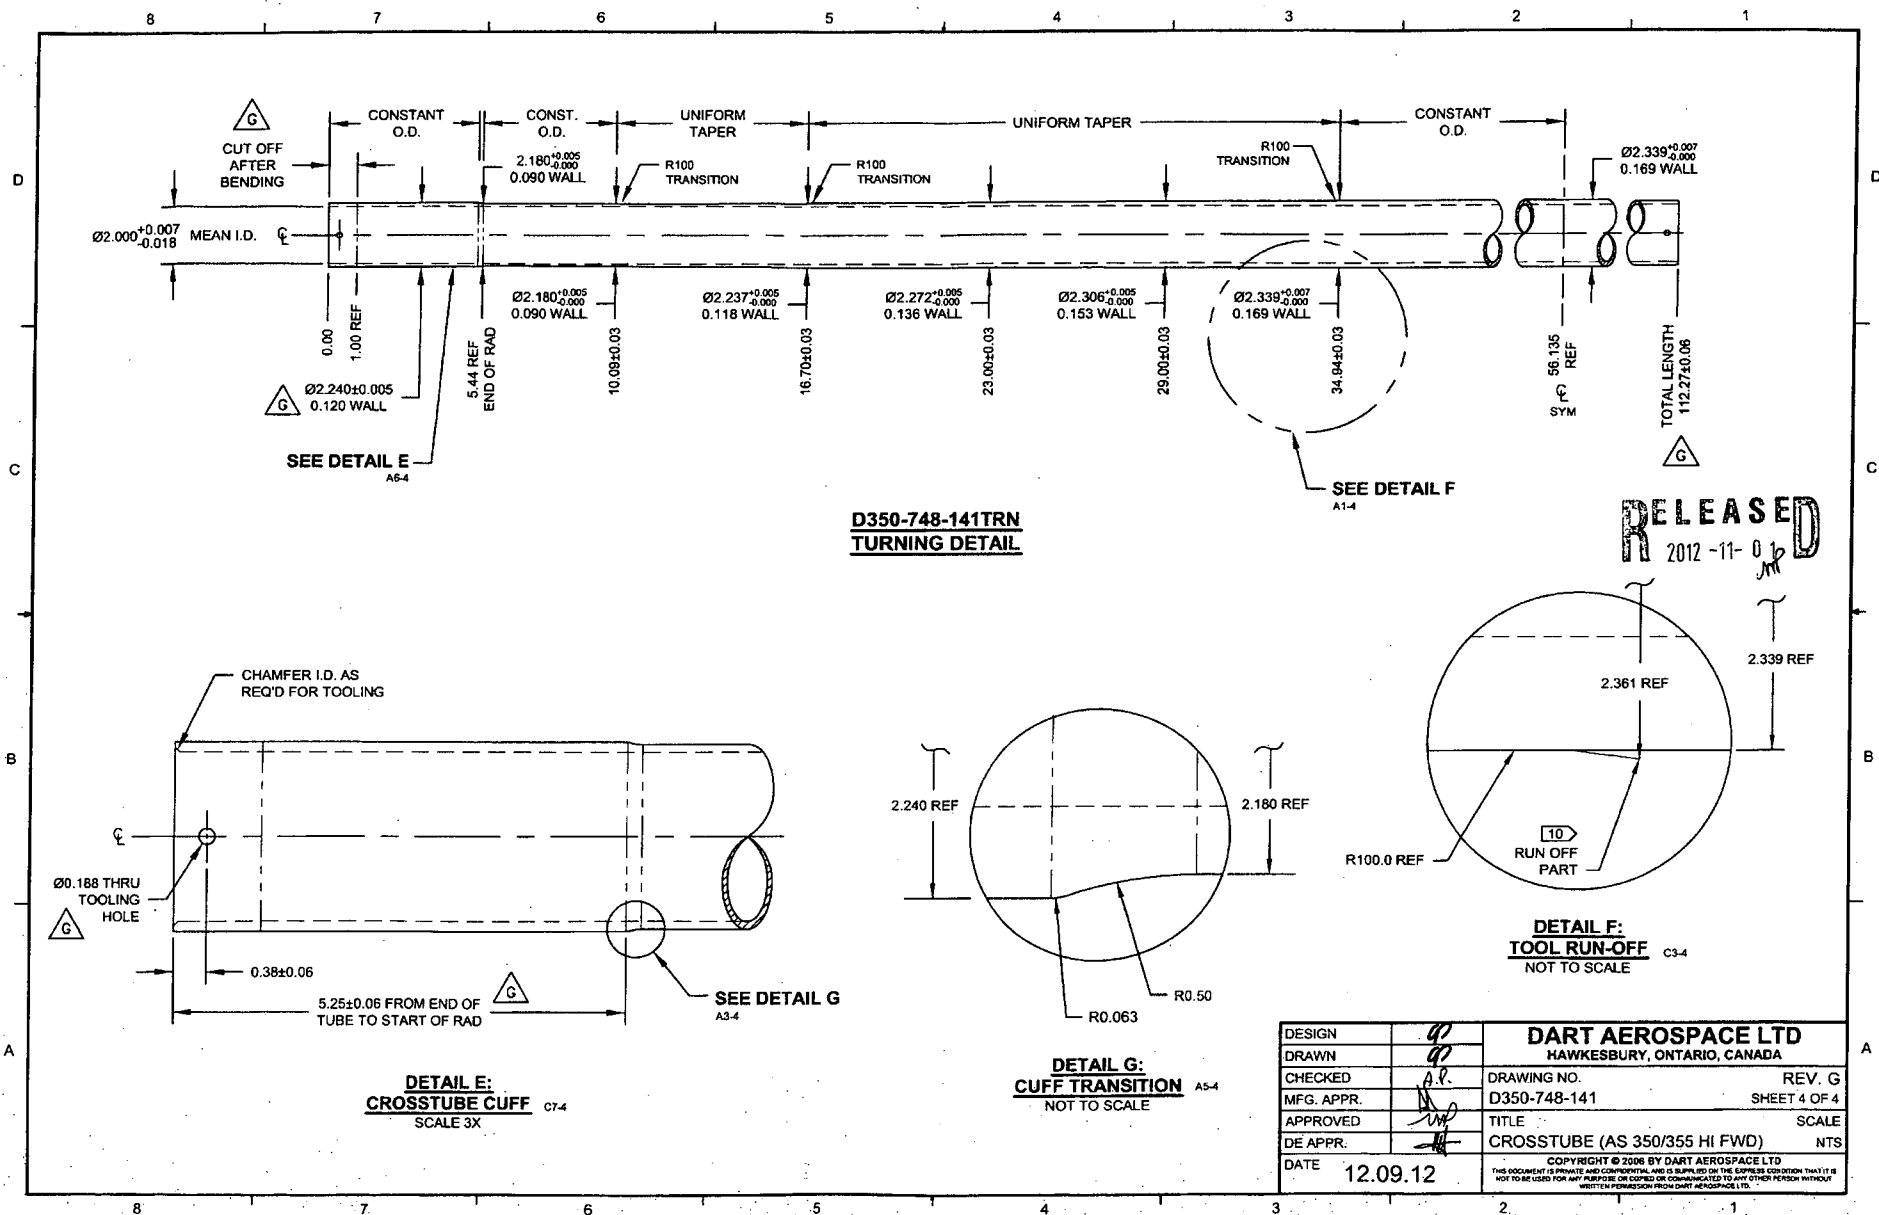

DART AEROSPACE LTD		Work Order:	
Description: Crosstube High Fwd (AS350/355)		Part Number:	D350-748-101
Inspection Dwg: D350-748-141 Rev: G			Page 1 of 1

Required Dimension	Min	Max
Height	23.12	23.38
1/2 Span	40.77	41.03
Angle	75	77
Total Span	81.55	82.05
Bending Passes	7	--
Crushing	--	7%
Twist	--	0.38

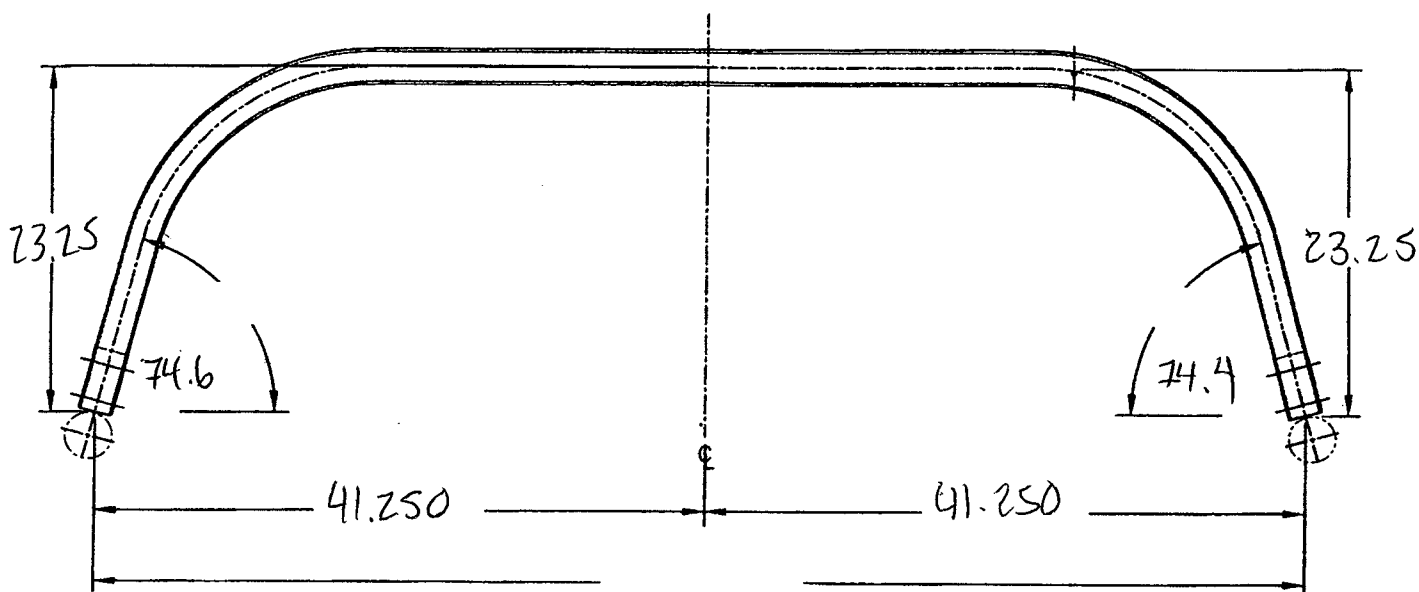

	Side A	Side B
Bending Passes	38	35
Crushing		
Comments		
twist = 0.023"		

QC15 Inspection	
Date	

Rev	Date	Change	Revised by	Approved
A	07.02.06	New Issue	KJ/JM	
B	10.08.23	Dwg Rev updated	KJ	
C	11.11.07	Dwg Rev updated	KJ	
D	12.04.16	Added bending, crushing & twist dimensions	KJ	
E	13.02.27	Dwg Rev updated	KJ	
F	14.02.13	Crushing & twist dimensions revised	KJ	

T
ACE

Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID PO26301

Purchase Order Date 10/29/2014

PO Print Date 10/30/2014

Page Number 2 of 3

From :
METCOR INC.
560 BOUL. ARTHUR SAUVE
SAINT-EUSTACHE, QC J7R 5A8
CA

VC-MET004

Ship To : DART AEROSPACE LTD
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name
Vendor Phone 450 473 1884

Ship To Contact
Ship To Phone
Ship Via: Dart Truck
Ship Acct:

Buyer Chantal Lavoie
Customer POID
Customer Tax # 10127-2607
Terms Net 30
Currency CAD
FOB FCA - (Free Carrier)

3	110172	D350-748-101 CROSSTUBE	10/31/2014	1.00	\$275.53	\$275.53
---	--------	---------------------------	------------	------	----------	----------

Yes
10/31/2014

HEAT TREAT CROSSTUBE AS PER QSI010 4.3
WITHIN 12H AFTER BENDING

Line Total: \$275.53

4	121505	D350-748-101 CROSSTUBE	10/31/2014	1.00	\$275.53	\$275.53
---	--------	---------------------------	------------	------	----------	----------

Yes
10/31/2014

HEAT TREAT CROSSTUBE AS PER QSI010 4.3
WITHIN 12H AFTER BENDING

8014-10-31

Line Total: \$275.53

5	110171	D350-748-101 CROSSTUBE	10/31/2014	1.00	\$275.53	\$275.53
---	--------	---------------------------	------------	------	----------	----------

Yes
10/31/2014

HEAT TREAT CROSSTUBE AS PER QSI010 4.3
WITHIN 12H AFTER BENDING

Note:

10/30/2014

METCOR INC.

560 BOUL. ARTHUR SAUVÉ
ST-EUSTACHE, QC J7R 5A8
Tel: 450-478-1880 / Fax: 450-491-6498

Reçu de livraison

Delivery Receipt

BON DE TRAVAIL Order	EXPÉDITEUR Shipper ID	BON D'EXPÉDITION Shipper
200096	1	85725

EXPÉDITION COMPLETE / Shipped Complete

CLIENT / Customer 215

DART AEROSPACE
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
Ph: 613-632-5200
Fax: 613-632-1053

LIVRÉ À / Shipped To

DART AEROSPACE
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
Ph: 613-632-5200
Fax: 613-632-1053



COMMANDE DU CLIENT Customer PO	BON DE LIVRAISON DU CLIENT Customer Shipper No	TYPE DE MATÉRIEL Material Type	DATE DE LA COMMANDE Order Date	TRANSPORTEUR Carrier
26301		Steel	2014/10/29	client
QUANTITÉ Quantity	Nb. PIÈCE Part No	NOM DE LA PIÈCE Part Name	DESCRIPTION DE LA PIÈCE Part Description	POIDS Weight

6 D350-748-101

CROSSTUBE

(1) D350-748-101 -113097

(1) D350-748-101 -113099

(1) D350-748-101 -110172

(1) D350-748-101 121505

(1) D350-748-101 110171

180

1 NIL

TYPE DE CONTENEUR Container Type	# DE CONTENEURS # Of Containers	COMMENTAIRES CONTENEUR Container Comments
NIL	1	

CERTIFICAT

EMPAQUETAGE Packing	
------------------------	--

QUANTITÉ EXPÉDIÉE / Quantity Shipped : 6

POIDS EXPÉDIÉ / Weight Shipped : 180,00

QUANTITÉ RESTANTE / Quantity Remaining : 0

POIDS RESTANT / Weight Remaining : 0,00

CERTIFICAT

QUANTITÉ EXPÉDIÉE / Quantity Shipped : 6

POIDS EXPÉDIÉ / Weight Shipped : 180,00

Signature:

Date:

METCOR INC.

560 BOUL. ARTHUR-SAUVÉ, ST-EUSTACHE, QC, J7R 5A8

Tél.: 450-473-1884

Télécopieur / Fax administration: 450-491-5498

Télécopieur / Fax production: 450 491-6454

Rapport d'Inspection**Inspection Report**

BON DE TRAVAIL order	CHARGEMENT load
200096	1

CLIENT / customer 215

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY

ON K6A 1K7

LIVRÉ À / shipped to:

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY

ON K6A 1K7

COMMANDE DU CLIENT customer po	BON DE LIVRAISON DU CLIENT customer shipper no.	MATÉRIEL material	MAÎTRE D'OEUVRE prime contractor	PROGRAM
26301		Steel		

SPÉCIFICATIONS DU PROCÉDÉ

processing specifications

STRESS REL

SAE AMS 2768/1 REV.E

EXIGENCE / requirement SPÉCIFICATIONS / specified TESTS EXÉCUTÉS / performed RÉSULTATS DE TESTS / results

Visual


QUANTITÉ quantity	POIDS weight	DESCRIPTION DES PIÈCES parts description
6	180	D350-748-101 CROSSTUBE (1) D350-748-101 -113097 (1) D350-748-101 -113099 (1) D350-748-101 110172 (1) D350-748-101 121505 (1) D350-748-101 110171 1 NIL

8/14-10-31

30 oct

COMMENTAIRES / comments

APPROUVÉ par / Approved by:




DATE: 2014-10-30

METCOR INC.

560 BOUL. ARTHUR-SAUVÉ, ST-EUSTACHE, QC, J7R 5A8

Tél.: 450-473-1884

Télécopieur / Fax administration: 450-491-5498

Télécopieur / Fax production: 450 491-6454

Certificat de Conformité Détaillé

Detailed Certificate of Compliance

BON DE TRAVAIL order	CHARGEMENT load
200096	1

CLIENT / customer 215

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY

ON K6A 1K7

LIVRÉ À / shipped to:

DART AEROSPACE

1270 ABERDEEN

HAWKESBURY

ON K6A 1K7

COMMANDE DU CLIENT customer po	BON DE LIVRAISON DU CLIENT customer shipper no.	MATÉRIEL material	MAÎTRE D'OEUVRE prime contractor	PROGRAM
26301		Steel		
SPÉCIFICATIONS DU PROCÉDÉ processing specifications				
STRESS REL				
SAE AMS 2759/1 REV.E				
EXIGENCE / requirement SPÉCIFICATIONS / specified TESTS EXÉCUTÉS / performed RÉSULTATS DE TESTS / results				
Visual				
QUANTITÉ quantity	POIDS weight	DESCRIPTION DES PIÈCES parts description		
6	180	D350-748-101 CROSSTUBE (1) D350-748-101 -113097 (1) D350-748-101 -113099 (1) D350-748-101 110172 (1) D350-748-101 121505 (1) D350-748-101 110171 (1) D350-748-101 113098 1 NIL		

COMMENTAIRES / comments

STRESS RELIEF 343C, 2 HRS

Le traitement thermique (TT) a été fait en utilisant des équipements en conformité avec AMS2759. Le TT a été fait tel que requis par AMS2759 et toutes les vérifications et les tests demandés ont été faites et documentés. Aucun changement n'a été faite par rapport au TT. On certifie que le matériel a été fabriqué, échantillonné, testé et inspecté en accord avec AMS2759 et le bon de commande et le matériel rencontre les exigences spécifiées.

Heat treatment (HT) was performed with equipment that meets the requirements of AMS2759. All HT operations were in compliance with AMS2759 and all verifications have been performed and documented. No unauthorized changes were performed in regards to the HT. We certify that the material was manufactured, sampled, tested and inspected in accordance with AMS2759 and the purchase order and was found to meet the requirements.

APPROUVÉ par / Approved by: Isabel Otero QA Technician  DATE: 2014-10-30



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID PO26611

Purchase Order Date 11/25/2014

PO Print Date 11/25/2014

Page Number 2 of 5

Order From:

VC-CAD002

Ship To: DART AEROSPACE LTD

CADORATH COATING
2150 LOGAN AVE.
WINNIPEG, MB R2R 0J2
CA

1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name

Vendor Phone 204 633 9420

Ship To Contact

Ship To Phone

Ship Via: Day & Ross collect

Ship Acct:

Buyer

Chantal Lavoie

Customer POID

Customer Tax # 10127-2607

Terms

Net 30

Currency

CAD

FOB

Destination-Collect

113097	D350-748-101	12/19/2014	1.00	\$803.42	\$803.42
--------	--------------	------------	------	----------	----------

CROSSTUBE

Yes

12/19/2014

FINISH: SAME AS ABOVE

Line Total: \$803.42

113098	D350-748-101	12/19/2014	1.00	\$803.42	\$803.42
--------	--------------	------------	------	----------	----------

CROSSTUBE

Yes

12/19/2014

FINISH: SAME AS ABOVE

Line Total: \$803.42

113105	D350-748-101	12/19/2014	1.00	\$803.42	\$803.42
--------	--------------	------------	------	----------	----------

CROSSTUBE

Yes

12/19/2014

FINISH: SAME AS ABOVE

Line Total: \$803.42

Note:

11/25/2014

2015-01-27

Packing Slip



Cadorath Coating

2150 Logan Avenue, Winnipeg, Manitoba R2R-0J2

Phone: (204) 633-9420 Fax: (204) 633-8033

INVOICE NUMBER:

S 74804

Sold To:

Dart Aerospace Ltd.

1270 Aberdeen St.

Hawksbury, ON K6A 1K7

ShipTo:

Net 2% Interest Per Month charged on Overdue Accounts.

Any claims for shortages, overcharges, or damaged goods must be made within seven (7) days from receipt of goods.

Customer Order #:	Date Received:	Terms:	G.S.T. #:	Ship Via:	Ship Date:
PO26611	Dec-31-2014	NET 30 DAYS	10071 6547 RT0001		Jan-22-2015

Item #	Qty	P/N & Description	
1	1 EA	CROSSTUBE	S/N 110171
		P/N d350-748-101	W/O 142527
2	1 EA	CROSSTUBE	S/N 110172
		P/N d350-748-101	W/O 142528
3	1 EA	CROSSTUBE	S/N 113097
		P/N d350-748-101	W/O 142529
4	1 EA	CROSSTUBE	S/N 113098
		P/N d350-748-101	W/O 142530
5	1 EA	CROSSTUBE	S/N 113062
		P/N D350-748-201	W/O 142531
6	1 EA	CROSSTUBE	S/N 113063
		P/N D350-748-201	W/O 142532
7	1 EA	CROSSTUBE	S/N 113067
		P/N D350-748-201	W/O 142533
8	1 EA	CROSSTUBE	S/N 110106
		P/N D350-748-201	W/O 142534
9	1 EA	CROSSTUBE	S/N 110108
		P/N D350-748-201	W/O 142535
10	1 EA	CROSSTUBE	S/N 121505
		P/N D350-748-101	W/O 142536
11	1 EA	CROSSTUBE	S/N 122288
		P/N D350-748-101	W/O 142537

SP15-01-27

**CERTIFICATE OF
CONFORMANCE**

**CADORATH PLATING CO. LTD.
2150 LOGAN AVENUE
WINNIPEG, MANITOBA R2J-0J1**

DATE: Jan-22-2015

CONSIGNED TO: Dart Aerospace Ltd.
1270 Aberdeen St.
Hawksbury, ON K6A 1K7

W/O #: 142536
INVOICE #: 74804

**CONTRACT OR
PURCHASE ORDER #** PO26611

DESCRIPTION: CROSSTUBE

QTY 1

P/N # D350-748-101


S/N # 121505

STRESS RELIEF BAKE HEAT CHART # 14-1216.MPI IAW ASTM-E-1444. CADMIUM PLATE IAW AMS-QQ-P-416C TYPE 2 YELLOW CLASS 1. FINAL MPI IAW ASTM-E-1444. EMBRITTLE RELIEF BAKE HEAT CHART # 15-38.

Sp15-01-27

CERTIFICATE: I certify that the items indicated here on have been inspected and tested and conform to all specifications and requirements detailed on the contract or purchase order.

Approved Inspector:



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID **PO27244**

Purchase Order Date 1/28/2015

PO Print Date 1/29/2015

Page Number 3 of 7

Order From :
SKYSERVICE
6120 MIDFIELD ROAD
MISSISSAUGA, ONTARIO L5P 1B1
CANADA

VC-SKY001

Ship To : DART AEROSPACE LTD
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name

Vendor Phone

905-678-5636

Ship To Contact

Ship To Phone

Ship Via:

Delivered

Ship Acct:

Buyer

Chantal Lavoie

Customer POID

Customer Tax #

10127-2607

Terms

Net 30

Currency

CAD

FOB

FCA - (Free Carrier)

6	113097	D350-748-101 CROSSTUBE	1/29/2015	1.00	\$0.00	\$0.00
---	--------	---------------------------	-----------	------	--------	--------

Yes

1/29/2015

SAME AS ABOVE

Line Total: \$0.00

7	113098	D350-748-101 CROSSTUBE	1/29/2015	1.00	\$0.00	\$0.00
---	--------	---------------------------	-----------	------	--------	--------

Yes

1/29/2015

SAME AS ABOVE

Line Total: \$0.00

8	121505	D350-748-101 CROSSTUBE	1/29/2015	1.00	\$0.00	\$0.00
---	--------	---------------------------	-----------	------	--------	--------

Yes

1/29/2015

SAME AS ABOVE

Line Total: \$0.00

SP15-01-29

Note:

1/29/2015

**skyservice****Work Order Traveler**
Sky Service F.B.O. Inc.

DOT APP 53-89 / EASA 145.7142 / BDA AMO 385

WO #: MWO21993	Customer: Dart Aerospace Ltd.	Dept: NDT YUL	Reference: PO: 27244
Descr:	PN:	S/N:	Qty: 1
Make:	Model:	Reg:	A/C S/N:
TSN: 0	CSN: 0	TSO: 0	

Task: UNSCHEDULED	Sequence: 1
--------------------------	-------------

Work Required:

CARRY OUT NDT ON THE FOLLOWING FWD CROSSTUBES
ID # D350-748-101
WORK ORDER ID'S # 110172, 110171, 113092, 113098, 121505

CARRY OUT NDT ON THE FOLLOWING AFT CROSSTUBES
ID # D350-748-201
WORK ORDER ID'S # 113063, 113062, 113062, 110106, 110108

Action Taken:	Date:	Initial/Stamp:
LIQUID PENETRANT INSPECTION CARRIED OUT ON ITEMS LISTED ABOVE IN ACCORDANCE WITH ASTM E1417M-13 ANY SUSPECT INDICATIONS VERIFIED BY EDDY CURRENT.	JAN 27 2015	
DAS 38 9-88 JAN 30 2015		

Description	Location	P/N	Qty	Batch	S/N Off	S/N On
LPI - ARDOR		970825E				
BLACK LIGHT		S/N: M-20142				
EDDY CURRENT		NORTEC 500,5				
		S/N: M20323 CAL. 11/NOV/2015				

SP15-01-29.

I certified that the maintenance described above has been performed in accordance with the applicable standard of airworthiness.

Signature:	ACA/SCA Stamp 	Date: JAN 27 2015
Name: RALF MELIKIAN		



Imron® 3.5 HG + High Gloss Polyurethane Topcoat (RH Quality)



GENERAL

DESCRIPTION

A high gloss 3.5 lbs/gal VOC conforming, low HAPS, polyurethane topcoat based upon unique Axalta formulations and resin technology. The resulting finish product provides a brush, roll or sprayable topcoat designed for use in any environment where long term color and gloss retention are desired.

SUGGESTED USES

As a high performance topcoat over suitable primers or properly prepared steel, galvanized steel, stainless steel, aluminum, concrete, concrete block, fiberglass, plastics and wood where:

- Long term color retention is desired
- Long term gloss retention is desired
- Compliance with 3.5 lbs VOC regulations is desired
- Use in corrosive or industrial marine environments is needed
- Application by brush, roll or spray is desired
- Excellent chemical resistance is desired
- Outstanding flexibility is needed
- Faster dry times are desired

COMPATIBILITY WITH OTHER COATINGS

- Aged Imron 3.5 HG + may be re-coated with itself following washing with clean, fresh water – no mechanical surface preparation is required.
- Imron 3.5 HG + can be applied over other Axalta coatings including, but not limited to Imron Industrial Strength primers and other Imron primers, Imron waterborne polyurethane copolymer coatings, Corlar® epoxies, Tufcote® acrylics, and Tufcote alkyd primers.
- Imron 3.5 HG + may be used over most aged and hard-cured coatings in good condition. Testing for lifting, bubbling and adhesion is recommended to assure compatibility with unknown coatings. Contact your Axalta representative for specific recommendations.

NOT RECOMMENDED FOR

Immersion service or floors

PERFORMANCE PROPERTIES

Abrasion & Mechanical	Excellent
Alkalis	Excellent
Humidity	Excellent
Solvents	Excellent
Color & Gloss Retention	Excellent
Acids	Excellent
Salts	Excellent
Weather	Excellent

The products referenced herein may not be sold in your market. Please consult your distributor for product availability.

COLOR

Imron 3.5 HG + consists of a mixing system utilizing 19 tints and 1 binder (3500P™) to specific mixing formulas. Select high-volume factory package colors are also available. Thousands of custom colors can be mixed.
